CAUTION:

HIGH CENTER OF GRAVITY - USE CAUTION WHEN MOVING CABINET

ONLY PERSONNEL TRAINED TO MOVE HEAVY EQUIPMENT SHOULD HANDLE THESE BATTERY SYSTEMS.

MOVE SLOWLY WHEN HANDLING. AVOID BOUNCING THE CABINET WHILE MOVING. THE CABINET COULD FALL FORWARD OR SIDEWAYS IF HANDLED ROUGHLY.

USE A FORKLIFT OR SIMILAR DEVICE WITH APPROPRIATE LIFTING CAPACITY TO LIFT THE CABINET.

AND COULD WEIGH AS MUCH AS 9,000 LBS PER CABINET OR MORE.

CABINET SYSTEMS ARE HEAVY

NOTE THE CENTER OF GRAVITY MEASUREMENT


STEPS FOR BATTERY CABINET INSTALLATION PROCEDURE

- TO HELP PREVENT DAMAGE, ALL PANELS FROM ALL BATTERY CABINETS SHOULD BE 1. LABELED TO THEIR PROSPECTIVE CABINET, REMOVED AND PUT ASIDE IN A SAFE LOCATION WHILE MOVING THE CABINETS TO FINAL INSTALL POSITION.
- INSTALL AND ALIGN THE FIRST CABINET, THEN EACH CABINET ADJACENT TO EACH OTHER. 2. REFER TO PAGE 3 FOR PROPER LINE UP.
- ROUTE THE POWER CABLES AS SHOWN ON SHEET 4. 3.
- INSTALL SIDE PANEL ONTO THE OPEN SIDES OF THE BATTERY CABINET. INSTALL THE 4. DOORS AND LOCK WHEN NOT OPEN FOR MAINTENANCE.
- THE CABINET MUST BE ANCHORED TO THE FLOOR FOR SEISMIC SENSITIVE AREAS. AND TO 5. MAINTAIN THE SEISMIC INTEGRITY OF THE BATTERY CABINET. ANCHORING HARDWARE IS NOT INCLUDED. CONTACT INTRAPACK TO PURCHASE ANCHORING HARDWARE

CAUTION: HIGH VOLTAGE, RISK OF ELECTRICAL SHOCK

FOLLOW ALL SAFETY PRECAUTIONS WHEN WORKING ON THIS SYSTEM

ALWAYS WEAR PROPER SAFETY EQUIPMENT INCLUDING EYE PROTECTION

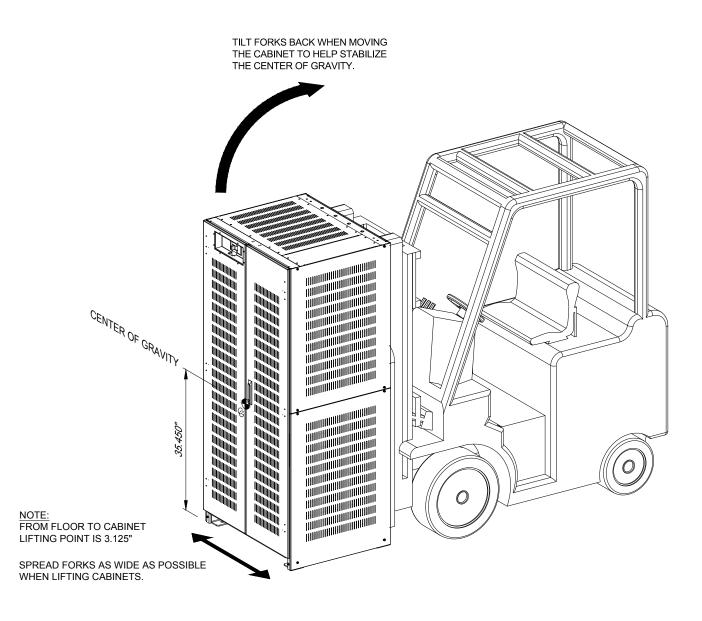

MOVING A BATTERY CABINET DO NOT LIFT THE CABINET HIGHER THAN NECESSARY TO CLEAR THE FLOOR WHEN MOVING


THE INFORMATION CONTAINED IN THIS DRAWING IS THE SOLE PROPERTY OF INTRAPACK INDUSTRIES INC. ANY REPRODUCTION IN PART OR WHOLE WITHOUT THE WRITTEN PERMISSION OF INTRAPACK INDUSTRIES INC. IS PROHIBITED.									
NO.	DATE	REVISION DESCRIPTION		10650 MARKISON ROAD	SYSTEM WE	EIGHT: 33,225	lbs		
			IntraPack	DALLAS, TX. 75238	JOB NO.	N/A	DATE:	01	
				PHONE: 214-348-7105 EMAIL: SALES@INTRAPACK.COM	QUOTE NO.	IPC20-1027	DRAWN BY:		
-	-			© INTRAPACK 2020	SCALE:	N.T.S.	APPR. BY:		

> IMPORTANT<

* REVIEW THE DRAWINGS AND READ ALL INFORMATION BEFORE PROCEEDING WITH MOVING AND INSTALLING THESE BATTERY CABINETS



/29/2021	ADJACENT REMOTE TOP TERMINAL BATTERY CABINET SYSTEM	1
VZ	DRAWING NO.	OF
	IP5-200P545-480-5-5D600-AR-JC	6

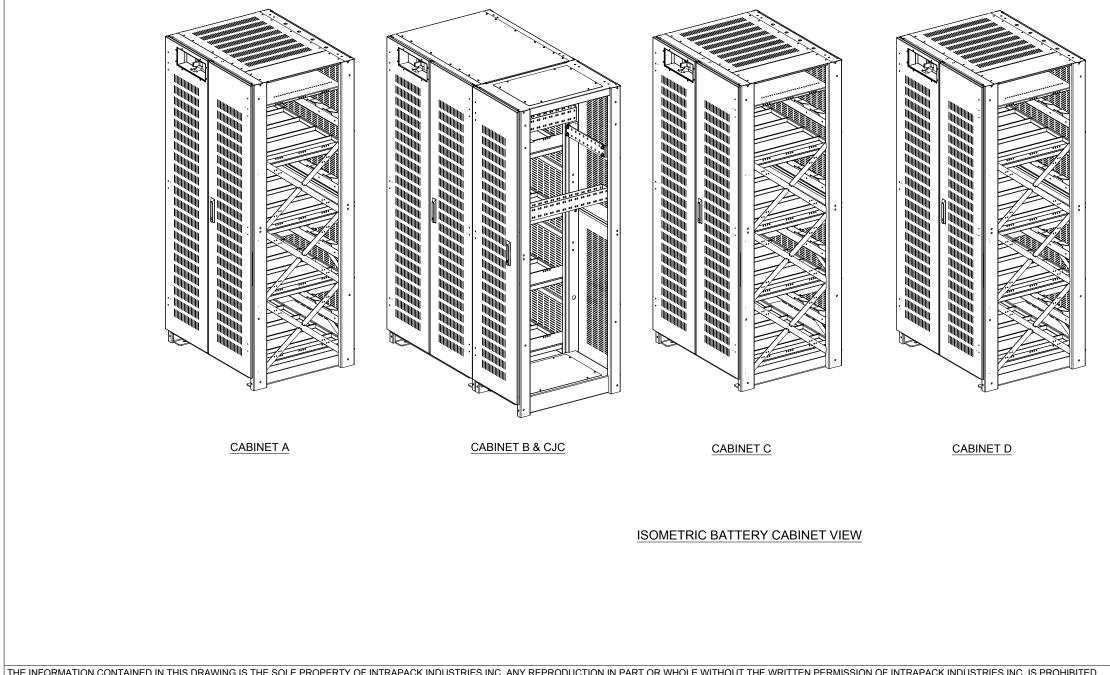


NO.	DATE	REVISION DESCRIPTION		B B		SYSTEM WEIGHT: 33,225 lbs			ADJACENT REMOTE TOP TERMINAL	2
			IntraPack	DALLAS, TX. 75238 PHONE: 214-348-7105	JOB NO.	N/A	DATE:	01/29/2021	BATTERY CABINET SYSTEM	OF
		L	WWW.INTRAPACK.COM	EMAIL: SALES@INTRAPACK.COM	QUOTE NO.	IPC20-1027	DRAWN BY:	VZ	DRAWING NO.	C
				© INTRAPACK 2020	SCALE:	N.T.S.	APPR. BY:		IP5-200P545-480-5-5D600-AR-JC	0

CAUTION: HIGH VOLTAGE, RISK OF ELECTRICAL SHOCK

• FOLLOW ALL SAFETY PRECAUTIONS WHEN WORKING ON THIS SYSTEM


ALWAYS WEAR PROPER SAFETY EQUIPMENT INCLUDING EYE PROTECTION



CABINET E




MEGAFLEX UPS BATTERY SKU MGD1000-5-49-ALT

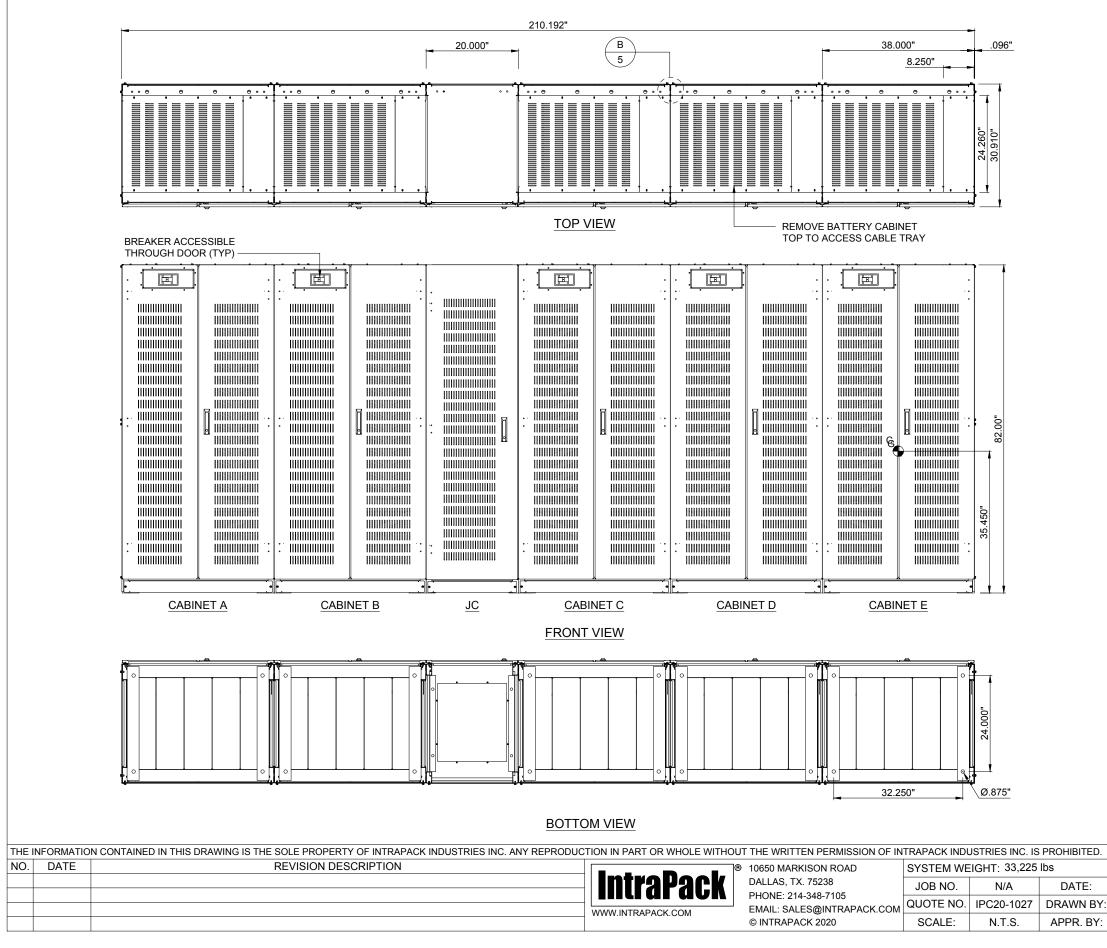

CAUTION: HIGH VOLTAGE, RISK OF ELECTRICAL SHOCK

FOLLOW ALL SAFETY PRECAUTIONS WHEN WORKING ON THIS SYSTEM

ALWAYS WEAR PROPER SAFETY EQUIPMENT INCLUDING EYE PROTECTION





MEGAFLEX UPS BATTERY SKU MGD1000-5-49-ALT


	ADJACENT REMOTE TOP TERMINAL	3	
01/29/2021	BATTERY CABINET SYSTEM	OF	
VZ	DRAWING NO.	0F	
	IP5-200P545-480-5-5D600-AR-JC	6	

DC POWER CABLES FROM CJC TO THE UPS PROVIDED BY OTHERS. REFER TO NEC FOR PROPER AWG SIZE

/1\


/2\

TERMINAL BLOCK TO TERMINAL BLOCK AND TERMINAL BLOCK TO UPS CONTROL WIRING WILL BE 16-20 GA STRANDED, PROVIDED BY OTHERS



CAUTION: HIGH VOLTAGE, RISK OF ELECTRICAL SHOCK

- FOLLOW ALL SAFETY PRECAUTIONS WHEN WORKING ON THIS SYSTEM
- ALWAYS WEAR PROPER SAFETY EQUIPMENT INCLUDING EYE PROTECTION

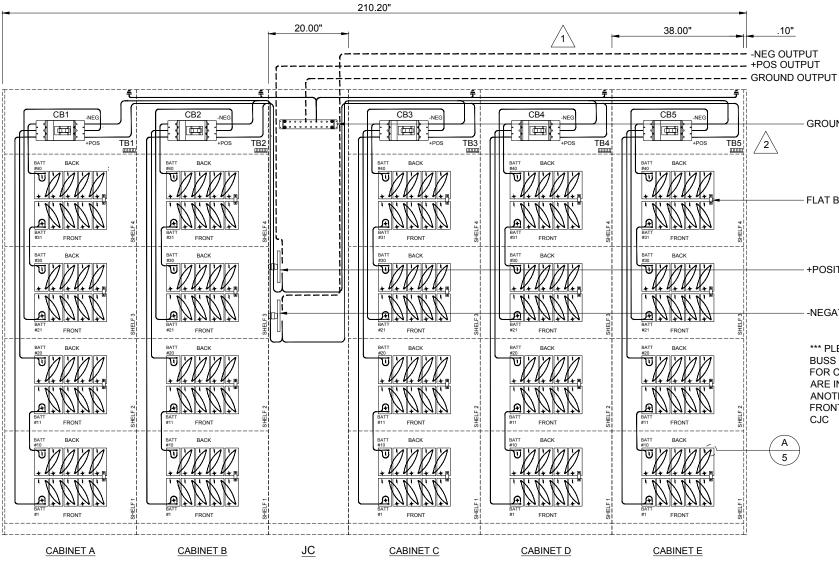

ELECTRICAL ILLUSTRATION

THE	INFORMATIC	IN CONTAINED IN THIS DRAWING IS THE SOLE PROPERTY OF INTRAPACK INDUSTRIES INC. ANY REPRODUC	CTION IN PART OR WHOLE WITHO	JT THE WRITTEN PERMISSION OF IN	ITRAPACK IND	USTRIES INC. IS	PROHIBITED.	
NO.	DATE	REVISION DESCRIPTION		B 10650 MARKISON ROAD	SYSTEM WE	EIGHT: 33,225	lbs	
			IntraPack	DALLAS, TX. 75238	JOB NO.	N/A	DATE:	01/2
				PHONE: 214-348-7105 EMAIL: SALES@INTRAPACK.COM	QUOTE NO.	IPC20-1027	DRAWN BY:	
				© INTRAPACK 2020	SCALE:	N.T.S.	APPR. BY:	

GENERAL NOTES:

- ONLY QUALIFIED TECHNICIANS SHOULD PERFORM 1 INSTALLATION OR MAINTENANCE OF THIS BATTERY SYSTEM.
- ALL TOOLS SHOULD BE INSULATED TO PREVENT ELECTRICAL 2. SHOCK.
- OPEN DISCONNECTS BEFORE INSTALLATION OR MAINTENANCE. 3.
- 4. CHECK DC VOLTAGE AT BATTERY OUTPUT AND UPS OUTPUT TO ENSURE PROPER POLARITY BEFORE MAKING FINAL CONNECTIONS.

GROUND BUS

- FLAT BRAID STRAP


+POSITIVE BUS

-NEGATIVE BUS

*** PLEASE NOTE THAT THE BUSS BARS ARE SHOWN APART FOR CLARITY ONLY, BUSS BARS ARE INLINE WITH ONE ANOTHER AND RUN FROM THE FRONT TO THE BACK OF THE CJC



29/2021	ADJACENT REMOTE TOP TERMINAL BATTERY CABINET SYSTEM	4
29/2021	BATTERT OABINET OTOTEM	OF
VZ	DRAWING NO.	0
	IP5-200P545-480-5-5D600-AR-JC	6

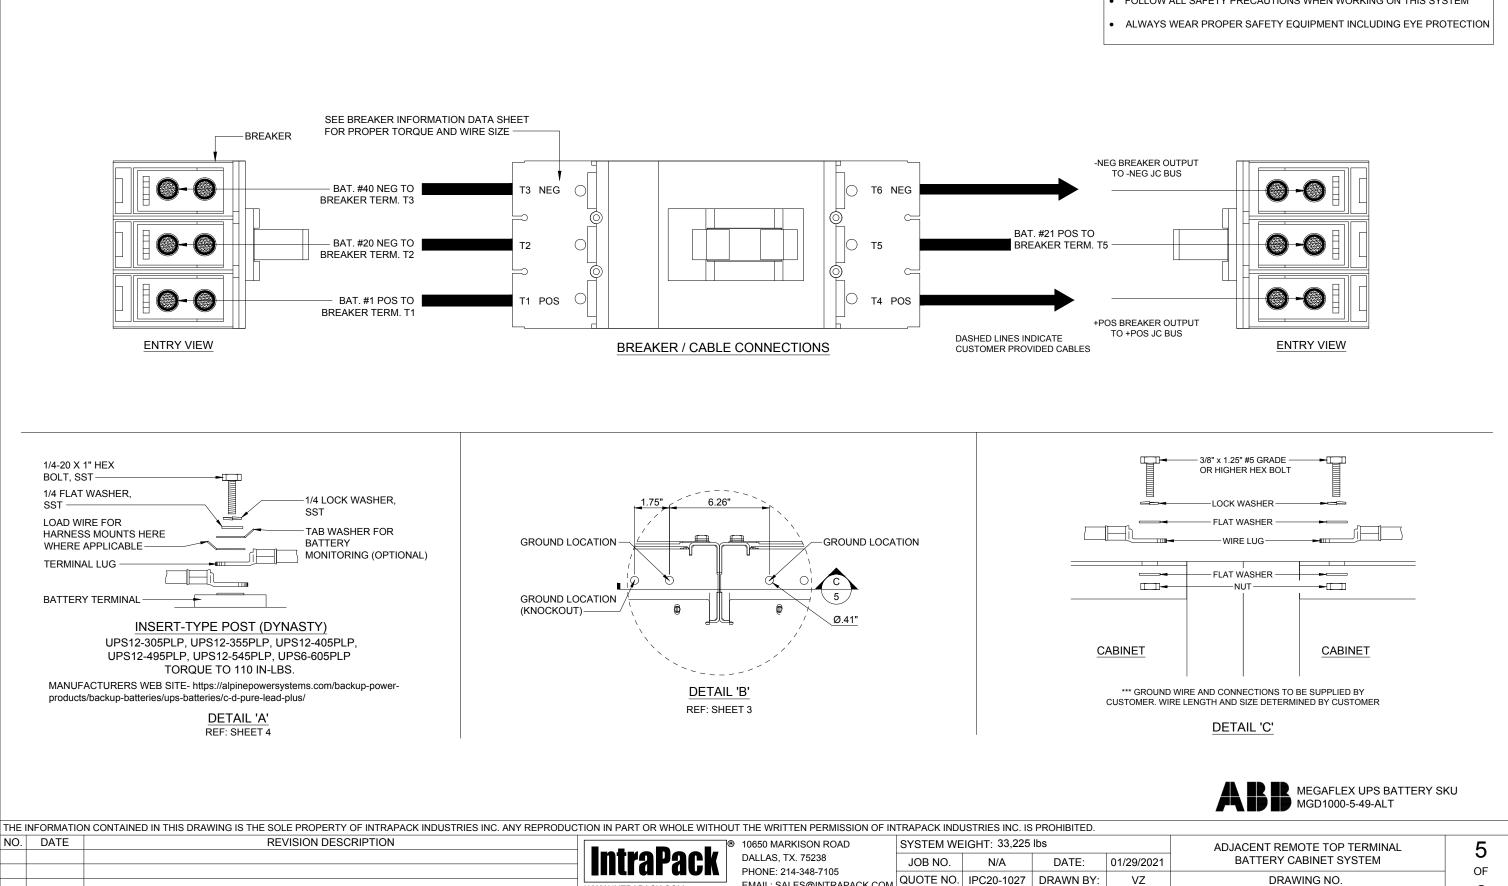

QUOTE NO. IPC20-1027 DRAWN BY: EMAIL: SALES@INTRAPACK.COM WWW.INTRAPACK.COM © INTRAPACK 2020 SCALE: N.T.S. APPR. BY:

CAUTION: HIGH VOLTAGE, RISK OF ELECTRICAL SHOCK

• FOLLOW ALL SAFETY PRECAUTIONS WHEN WORKING ON THIS SYSTEM

IP5-200P545-480-5-5D600-AR-JC

6

